Ft. Lowell / Campbell Intersection Improvements

City of Tucson / Contract No.: 100350

Two-Week Look Ahead Project Schedule (assumes no conflicts)

Falcone Brothers & Associates, Inc.

June - July 2010

	S	S	M	T	W	TH	F	S	S	M	T	W	TH	F	S	S	M	T	W	TH	F	S	S	M	T
	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6
ACTIVITY																									
Safety / Traffic Control																									
SWPPP																									
Surveying																									
Quality Control																									
PHASE 1: a) EB Ft. Lowell (West & East of Campbell)(South half) b) SB Campbell (North & South of Ft. Lowell)(West half)																									
Temp Traffic Signal																									
AC Milling																									
Water - Segment 2																									
Soil Cement Removal - Campbell																									
Concrete Removals																									
Storm Drain System																									
Electrical / Signal																									
Rough Grading																									
Concrete Work																									
Finish Grading																									
ABC																									
AC Paving (Mix #1)																									

Schedule subject to change

Ft. Lowell & Campbell Intersection Improvements
City of Tucson Department of Transportation
Contract No.: 100350
June 2010 Update

Falcone Brothers & Associates, Inc.

ACTIVITY	May-10	Jun-10	Jul-10	Aug-10	Sep-10	Oct-10	Nov-10	Dec-10	Jan-11	Feb-11
General										
Safety / Traffic Control										
Mobilization										
SWPPP										
Surveying										
Sewer Flow Management Plans										
Quality Control										
PHASE 1:										
Sewer DIP Change Out - West										
Water / Sleeve Services - Segment 1										
Temp Traffic Signal										
AC Milling										
Water - Segment 2										
Soil Cement Removal - Campbell										
Concrete Removals										
Storm Drainage System										
Electrical / Signal										
Rough Grading										
Concrete Work										
Finish Grading										
ABC										
AC Paving (Mix #1)										
Phase 1 Complete										
PHASE 2:										
Switch Temp Traffic Signal										
Sewer DIP Change Out - East										
Water - Segment 3 @ Intersection										
AC Milling										

KEY:
original
June 2010 update
New activity

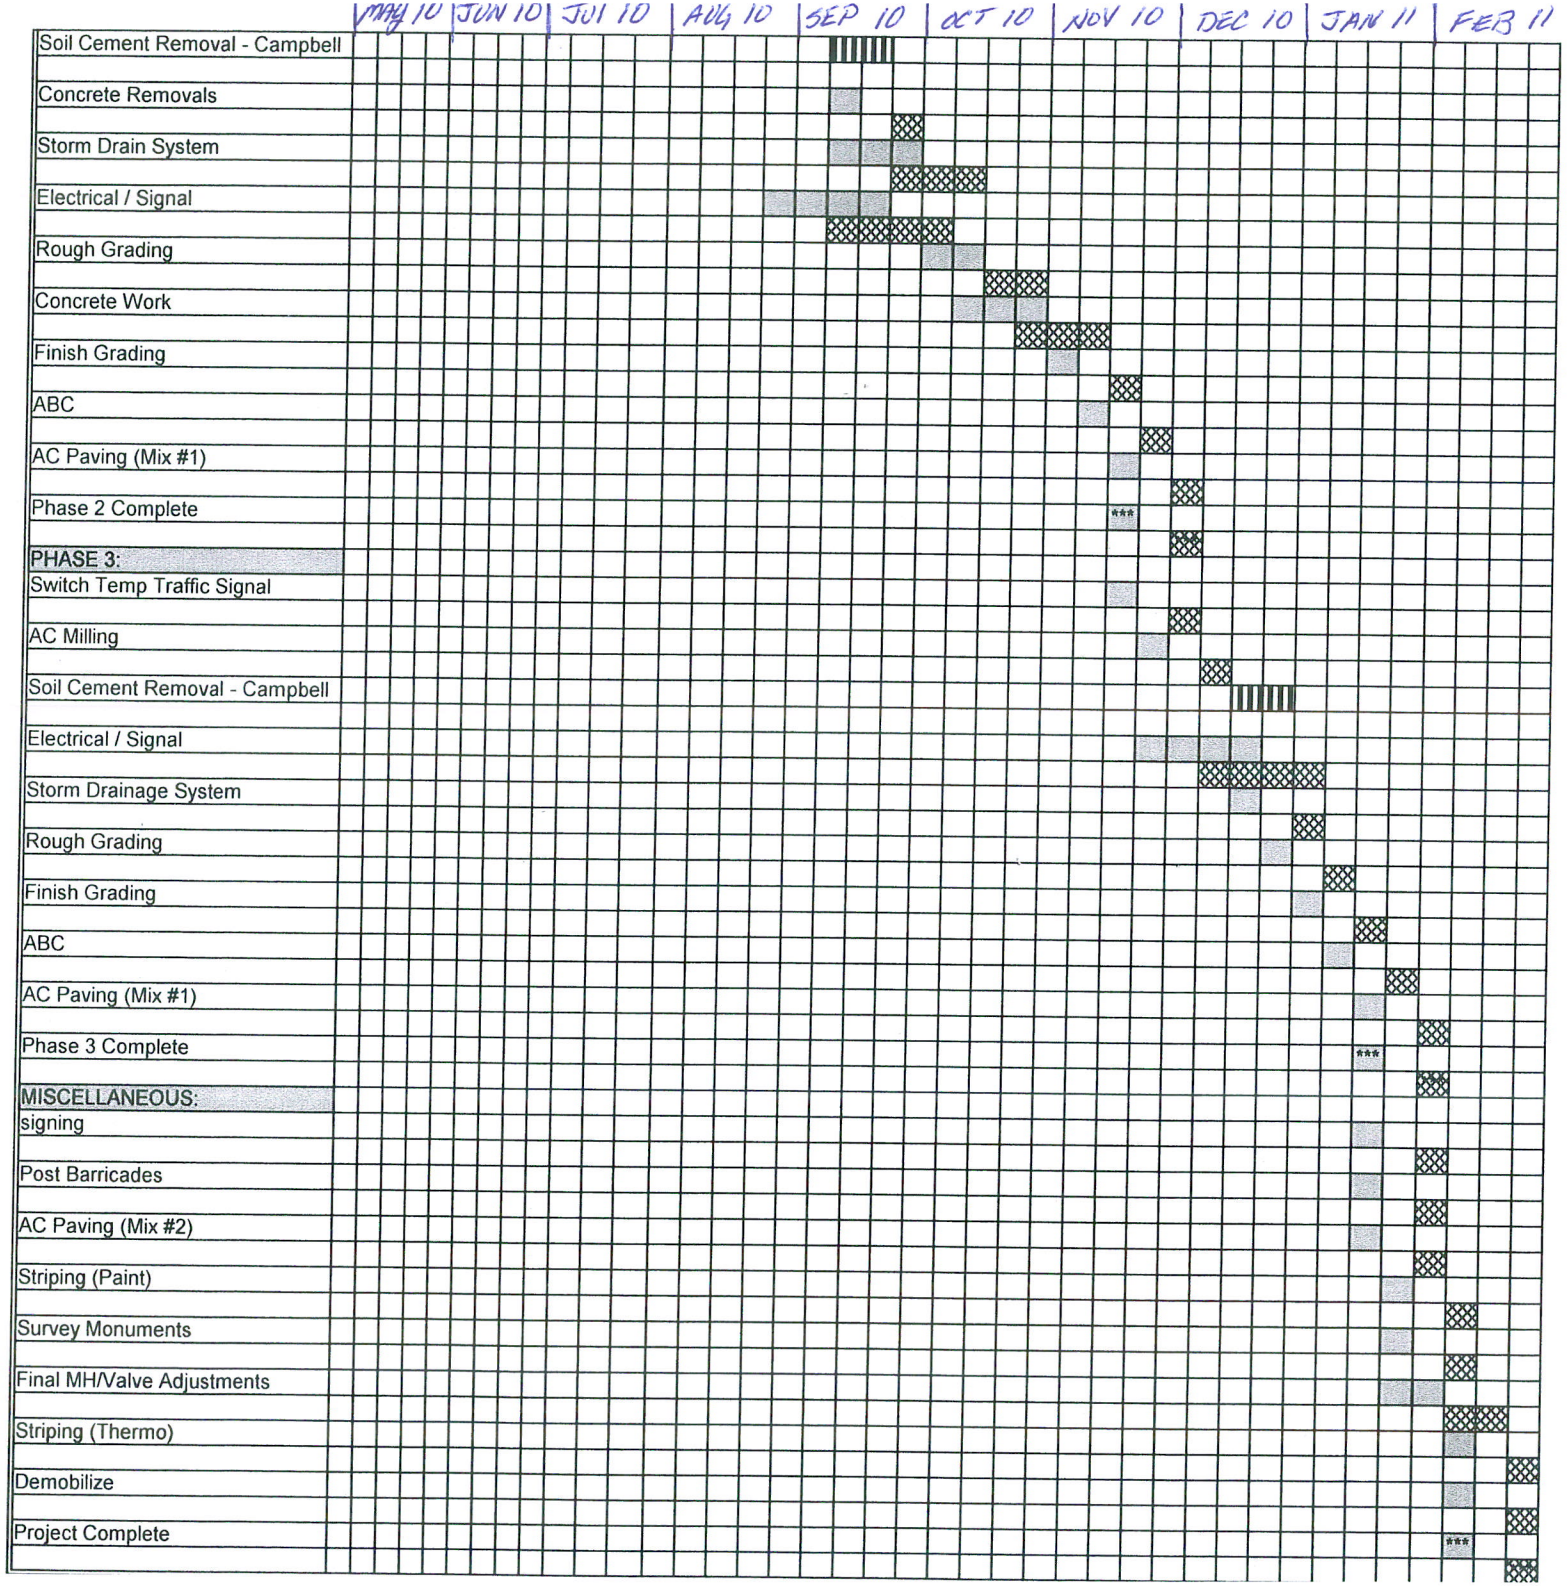
MAY 10
JUN 10
JUL 10
AUG 10
SEP 10
OCT 10
NOV 10
DEC 10
JAN 11
FEB 11
Soil Cement Removal - Campbell
Concrete Removals
Storm Drain System
Electrical / Signal
Rough Grading
Concrete Work
Finish Grading
ABC
AC Paving (Mix #1)
Phase 2 Complete
PHASE 3:
Switch Temp Traffic Signal
AC Milling
Soil Cement Removal - Campbell
Electrical / Signal
Storm Drainage System
Rough Grading
Finish Grading
ABC
AC Paving (Mix #1)
Phase 3 Complete
MISCELLANEOUS:
signing
Post Barricades
AC Paving (Mix #2)
Striping (Paint)
Survey Monuments
Final MH/Valve Adjustments
Striping (Thermo)
Demobilize
Project Complete
